

Monthly Status Report

Reporting Period
June 2024

1. Introduction

1.1 Project Overview

The Kicking Horse Canyon Project – Phase 4 (KHCP4) is located on the Trans-Canada Highway approximately 4 km east of the Highway 95 junction at Golden BC. It is the final phase of the 26 km-long Kicking Horse Canyon Project which has been incrementally improving the highway to a modern four lane standard at a 100 km/h design speed, including bridge replacements and natural hazard reduction features to improve safety and reliability. The scope of work includes:

- Widening 4 km of two lane and 0.8 km of three lane highway to four lanes;
- Highway realignment to a 100 km/h design speed;
- Installation of median barrier, wildlife exclusion fencing and passages;
- Provision of snow avalanche and rock fall hazard reduction measures; and
- Shoulder widening for cyclists.

Construction of the fourth and final phase to complete the remaining – and most difficult – 4.8 kilometres is expected to be substantially complete in winter 2023-24.

Additional information and updates about the Project can be found on the Project’s website <https://www.kickinghorsecanyon.ca/>

1.2 Project Delivery

Transportation Investment Corporation, a provincial Crown corporation, is delivering and overseeing this \$601 million Project. The Project is being delivered under B.C.'s Community Benefits Agreement and the Project workforce is being provided by B.C. Infrastructure Benefits Inc. (BCIB).

The Project is cost-shared, with the Government of Canada contributing \$215 million.

Kicking Horse Canyon Constructors (KHCC) was selected to design and construct the fourth and final phase of the Kicking Horse Canyon Project near Golden.

The Project is a multi-phase Project to improve safety and mobility over approximately 26 kilometres of two-lane highway. Three phases of work have been completed. The fourth and final phase to transform the remaining section of about 4.8 kilometres is under construction.

1.3 Project Goals

Based on the Ministry of Transportation and Infrastructure's mandate six primary goals have been identified for the Project:

Transportation: Improve highway safety, capacity, and reliability of the highway corridor.

Financial: Plan and deliver the Project that meets the approved scope, schedule and budget targets cost effectively.

Environment: Reduce wildlife collision rates and minimize impacts on future wildlife movements.

Economic Development: Support the growth of the local and regional economy by improving highway safety and reliability and assist the efficient movement of people and goods along the Project corridor.

Social and Communities: Engage with Indigenous Communities, local communities, and key stakeholders to identify opportunities, issues and information pathways that will inform the delivery of the Project.

Deliverability: Constructable and operable.

2. Project Update

2.1 Project Dashboard

		Objectives	Project Status	Comments
Project Delivery	Scope	Meet the approved scope.	●	<ul style="list-style-type: none"> The Project includes the widening of 4.8km of Highway 1 to a 4-lane 100km/h standard and is being delivered within the approved scope.
	Schedule	Delivered within the approved schedule.	●	<ul style="list-style-type: none"> The Project successfully achieved Substantial Completion on November 30, 2023.
	Budget	Delivered within the approved budget. Total Project budget is \$601 million.	●	<ul style="list-style-type: none"> Project spending for the month of June 2024 is \$2.49 million. Project spending to date is \$587.4 million. Total Federal Recoveries are \$215.2 million. The Project is forecast to be delivered within budget.
	Safety	Take every reasonable step to ensure that our work is performed safely and in compliance with all applicable safety regulations, and in accordance with government policy.	●	<ul style="list-style-type: none"> Monitored the implementation of the health and safety program and performed site visits. zero (0) lost time injuries on the Project to date. Lost Time Injury Frequency Rate (LTIFR) for the Project is zero (0), which is less than the WorkSafeBC 2022 rate of 1.7* for Heavy Construction (Bridge, Overpass, or Viaduct Construction or Repair). <i>* Injury rate data reflects Large Employer 100+ Person Years employer size.</i>
	Quality	Implement an effective Quality Management System.	●	<ul style="list-style-type: none"> One (1) quality audit was conducted for the month of June.
	Environmental	Ensure our work is performed in an environmentally responsible manner.	●	<ul style="list-style-type: none"> Ongoing reviews for submission packages. No environmental site visit conducted in June; one is scheduled for early July.
	Archaeology	Ensure the work is performed in a manner that meets the standards of the Heritage Conservation Act.	●	<ul style="list-style-type: none"> All archaeology work completed on the Project.
	Design and Construction	Provide design and technical oversight, coordinate and manage activities on site, and conduct compliance reviews.	●	<ul style="list-style-type: none"> Oversight of Design-Build-Agreement (DBA) Project work. Compliance reviews during construction. Ongoing traffic management and active traffic monitoring during construction.
	Community Benefits	Work collaboratively with BC Infrastructure Benefits Inc. (BCIB) to successfully implement the Community Benefits Agreement (CBA).	●	<ul style="list-style-type: none"> Ongoing coordination and collaboration with BCIB to implement the CBA. Discussions regarding current and future Project workforce requirements continue to progress.

		Objectives	Project Status	Comments
Partners/Stakeholders	First Nations	Continue to build and maintain a positive collaborative working relationship.	●	<ul style="list-style-type: none"> The Project Team continues to collaborate with First Nations on key environmental values. Targets for indigenous contracting opportunities have all been achieved.
	Third Parties	Continue to build and maintain positive relationships and secure agreements with Project partners and other third parties.	●	<ul style="list-style-type: none"> Regular communication and coordination with Canadian Pacific Kansas City (CPKC).
	Public and Stakeholder Engagement	Continue to build and maintain positive relationships with the community and other stakeholders.	●	<ul style="list-style-type: none"> Ongoing work to enhance quality and reliability of traffic notifications. Regular website and social media updates including highway status calendar and stakeholder notices.

Status	Description
●	Managing critical issues, negotiating resolution; action required immediately
●	Managing some issues, negotiating resolution; action required in the near term
●	Managing day to day operations

3. Project Documents and Achievements to Date

Project Delivery	Project Planning and Development	<ul style="list-style-type: none"> • Business Case Supplemental Memo (2019) • Cost Report (2019) • Risk Report (2019) • Executed Design-Build-Agreement (November 2020)
	Environmental	<ul style="list-style-type: none"> • Environmental Synopsis Report (2016) • Various Environmental Reports (2005 – 2016)
	Archaeology	<ul style="list-style-type: none"> • Heritage Inspection Permit 2019-0208 (2019) • Archaeological and Heritage Resource Management Plan (AHRMP)_(August 2020) • Site Alteration Permit 2020-0297 (October 2020) and subsequent amendments
	Community Benefits	<ul style="list-style-type: none"> • Community Benefits Agreement (July 2018) • BCIB Health and Safety Program (March 2020) • BCIB-AIRCC Enabling Agreement (May 2020) • Project Definition: Trans Canada Highway #1 – Kamloops to Alberta Border 4-Laning Project (March 2020) • BCIB-Contractor Agreement (March 2020) • BCIB-Subcontractor Agreement (March 2020)
	Third Parties	<ul style="list-style-type: none"> • Contribution Agreement – Government of Canada (2017)

4. Monthly Highlights and Three Month Lookahead

4.1 Safety

Scope:	<ul style="list-style-type: none"> Establish Occupational Health and Safety (OH&S) Project delivery objectives and performance measures. Manage Project OH&S activities and monitor performance metrics. Ensure the Project complies with relevant WorkSafeBC regulations and government requirements. Outline relevant health and safety management processes and activities.
Monthly Highlights:	<ul style="list-style-type: none"> No safety audit was scheduled in June. Two (2) first aid incidents, no lost time, and no property/equipment damage incidents for the month of June. Zero (0) lost time injuries on the Project to date. Lost Time Injury Frequency Rate (LTIFR) for the Project is zero (0), which is less than the WorkSafeBC 2022 rate of 1.7* for Bridge, Overpass, or Viaduct Construction or Repair (subsector Heavy Construction). <i>*Injury rate data reflects Large Employer 100+ Person Years employer size.</i>
Three Month Lookahead:	<ul style="list-style-type: none"> Maintain Province's Safety Management Plan for implementation as part of the Design-Build Agreement to align with KHCC, Transportation Investment Corporation (TIC), the Owner's Engineer (OE) and Ministry of Transportation and Infrastructure requirements. Conduct orientation and safety training for onsite personnel as required. Conduct surveillance audits of KHCC's safety management performance.

4.2 Quality

Scope:	<ul style="list-style-type: none"> Establish quality objectives and performance measures. Monitor relevant quality management performance metrics. Manage Project quality management activities.
Monthly Highlights:	<ul style="list-style-type: none"> One (1) Non-conformity Reports (NCRs) received for the month of June. To date there have been a total of 120 NCRs (zero (0) open and 120 closed). A quality site visit was conducted on June 11th, no issues were reported.
Three Month Lookahead:	<ul style="list-style-type: none"> Oversee quality of KHCC work onsite. Record and distribute daily observation reports of work onsite. Review KHCC quality records for compliance to the DBA. Conduct monthly audits of KHCC quality processes. Prepare for and review Total Completion submissions.

4.3 Environmental

Scope:	<ul style="list-style-type: none"> • Complete environmental reviews of KHCC’s submissions. • Support communications team with stakeholder engagement. • Conduct site surveillance and provide environmental support to Project as and when needed. • Conduct Project closure review documentation management process.
Monthly Highlights:	<ul style="list-style-type: none"> • Reviewed KHCC submissions. • No site visit in June. Site visit planned for early July. • Coordinate with the Ministry of Transportation and Infrastructure on exclusion fence considerations.
Three Month Lookahead:	<ul style="list-style-type: none"> • Continue review of KHCC’s environmental submissions. • Conduct site environmental surveillance and final site walkthrough. • Continue collaboration with the Golden District Rod and Gun Club and the Ktunaxa Nation Council on bighorn sheep monitoring through to the project end in 2024.

4.4 Archaeology

Scope:	<ul style="list-style-type: none"> • Managing, directing, and undertaking all archaeological work, including Archaeology Impact Assessment (AIA), Systematic Data Recovery (SDR), and monitoring. • Providing the Province and KHCC with information for the management of archaeological and heritage resources. • Responding to chance archaeological or heritage finds.
Monthly Highlights:	<ul style="list-style-type: none"> • All archaeology work completed on the Project.
Three Month Lookahead:	<ul style="list-style-type: none"> • N/A

4.5 Design and Construction

Scope:	<ul style="list-style-type: none"> • Travel demand forecasting, traffic operations modelling, traffic data collection, and other related engineering services in support of the traffic management regime proposed for the Project. • Provide technical support to the Project team during the review of contractor submittals. • Oversight of DBA Project work. • Compliance reviews during construction. • Establish agreements with other jurisdictions for provision of services along the alternate route.
---------------	--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------

Monthly Highlights:	<p>Construction activities during the month included:</p> <ul style="list-style-type: none"> • Drainage work installation, Bighorn sediment basin, work on Pronghorn cut, snow fence installation at Caribou, ungulate guard installation at 5 Mile laydown area, cleanup at 10 Mile laydown area, and mitigation of pending deficiencies. • Monitoring daytime and early morning 2 hour closures. • Inspections of Wildlife Exclusion Fencing installations. • Monitored asset performance, and identifying deficiencies. • Ongoing review of handover submission packages.
Three Month Lookahead:	<ul style="list-style-type: none"> • Monitor slope survey works. • Undertake site surveillance, inspections, and audits by Project team, including OE Lead Engineer, OE Quality Manager, and OE Safety Advisor. • Monitor KHCC traffic management performance through site. • Begin process to add the Project to the Concession Agreement. • Alternate route signage removal (expected July 2024) • Ongoing landscaping, wildlife fencing, and drainage works across the Project.

4.6 First Nations

Scope:	<ul style="list-style-type: none"> • Fulfill Province’s duty to consult and accommodate Indigenous communities and facilitate engagement and collaboration with communities on environmental and socio-economic interests.
Monthly Highlights:	<ul style="list-style-type: none"> • No activities for the month of June.
Three Month Lookahead:	<ul style="list-style-type: none"> • Continue regular meetings with First Nations, including the Pespesellkwe, Ktunaxa, and Shuswap Indian Band.

4.7 Third Parties

Scope:	<ul style="list-style-type: none"> • Develop utilities and rail agreements as required. • Secure local and regional government approvals as required.
Monthly Highlights:	<ul style="list-style-type: none"> • Continued regular communication and coordination with CPKC.
Three Month Lookahead:	<ul style="list-style-type: none"> • Continue implementation of Protocol Agreement. • Coordinate construction activities with CPKC.


4.8 Public and Stakeholder Engagement

Scope:	<ul style="list-style-type: none"> • Manage ongoing public and stakeholder communications and engagement.
---------------	--------------------------------------------------------------------------------------------------------------------------

Monthly Highlights:	<ul style="list-style-type: none"> • Released monthly Project newsletter. • Responded to 7 public/stakeholder inquiries related to the Project progress.
Three Month Lookahead:	<ul style="list-style-type: none"> • Oversight of KHCC’s communication and public engagement obligations and activities. • Completion of retrospective video of Project. • Build awareness of construction and traffic management activities with media info bulletins/interviews, website updates, newsletters and advisories, and social media. • Continue direct dialogue with key stakeholders.

5. Schedule

The following schedule depicts deliverables, milestones and associated dates and timelines for the implementation phase of the Project, as well as anticipated construction timelines.

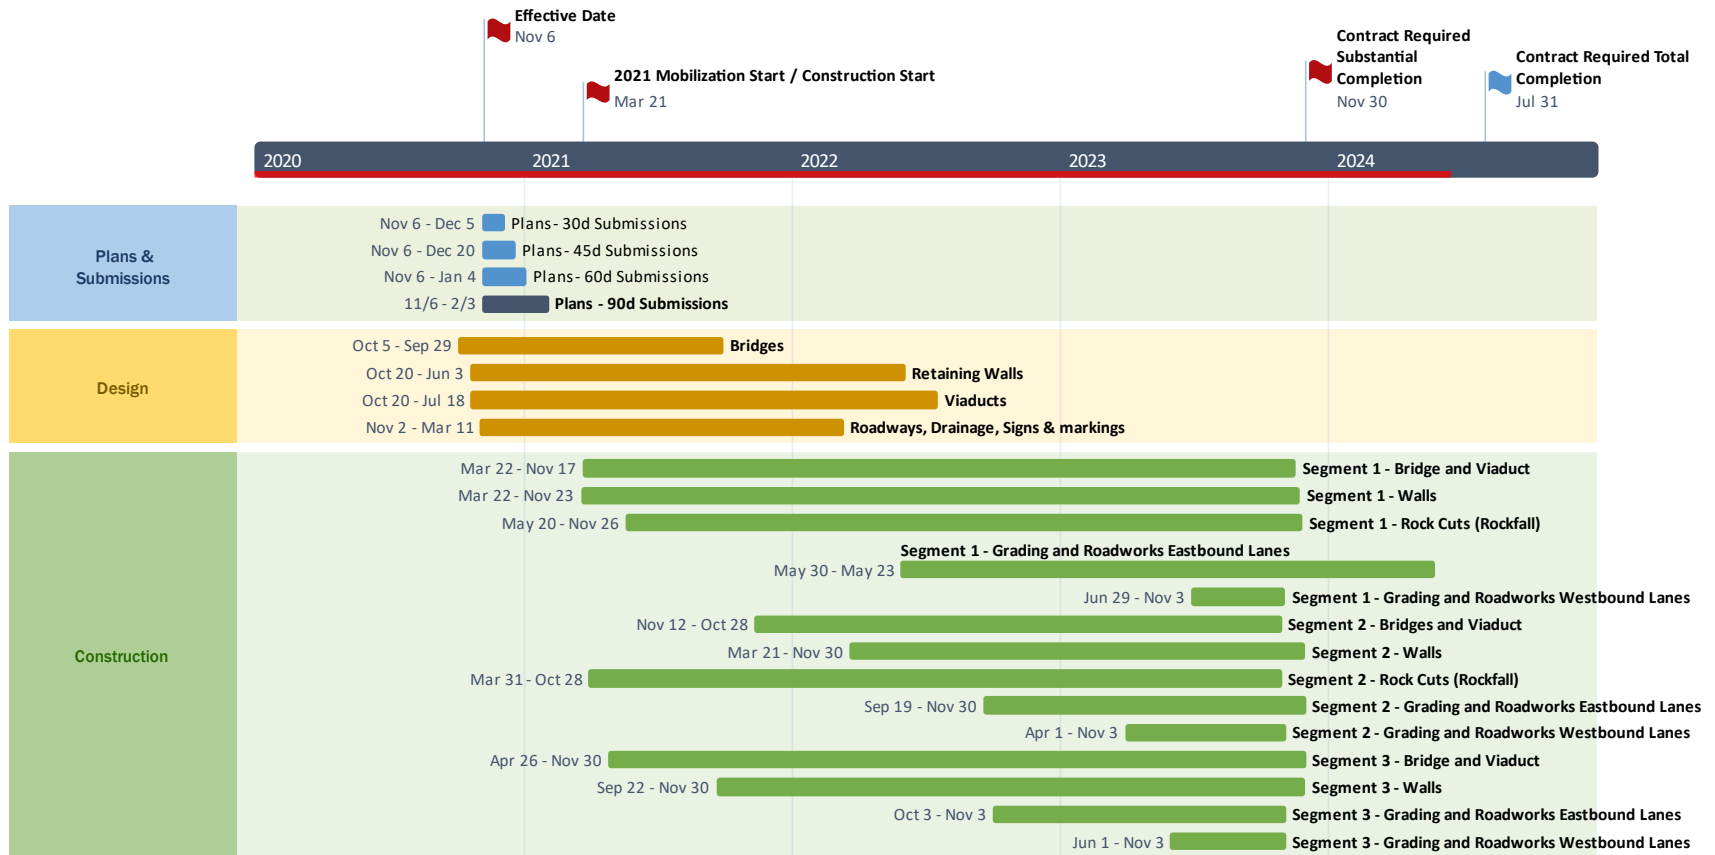

6. Project Photos



Figure 1: Hydroseeding complete at Pronghorn Cut – June 4, 2024



Figure 2: Cut 2 mesh adjustments – June 26, 2024



Figure 3: Ditch works at Caribou Wall area – June 21, 2024



Figure 4: Snooper truck working at Marmot Viaduct – June 25, 2024



Figure 5: Wildlife Exclusion Fence at Cut 3 – June 19, 2024
